Happy Valley Elementary / Middle School

ID	Task Name	Start	Finish
1	**GENERAL**	**Mon 4/30/07**	**Tue 9/2/08**
2	CM/GC Contract Selection	Mon 4/30/07	Mon 4/30/07
3	Mobilization	Tue 5/1/07	Thu 6/14/07
4	Last Day of School '06/'07	Fri 6/15/07	Fri 6/15/07
5	First Day of School '07/'08	Tue 9/4/07	Tue 9/4/07
6	Last Day of School '07/'08	Wed 6/11/08	Wed 6/11/08
7	First Day of School '08/'09	Tue 9/2/08	Tue 9/2/08
8	**SITEWORK**	**Tue 6/19/07**	**Tue 11/11/08**
9	Relocate Modulars	Mon 6/25/07	Mon 7/2/07
10	Demolish Existing Church	Tue 6/19/07	Mon 6/25/07
11	Site Rough Grading	Mon 6/25/07	Mon 7/16/07
12	Parking Lot Construction (Temporary Configuration)	Tue 7/10/07	Fri 8/31/07
13	Site Utilities	Tue 7/24/07	Tue 9/18/07
14	Demo of Existing Elementary School	Tue 7/1/08	Tue 8/26/08
15	Balance of Sitework & Paving	Mon 5/26/08	Fri 10/10/08
16	Remove Modulars	Tue 7/1/08	Mon 7/14/08
17	New Athletic Fields	Wed 8/6/08	Tue 11/11/08
18	**NEW ELEMENTARY SCHOOL**	**Tue 7/10/07**	**Fri 8/22/08**
19	Earthwork	Tue 7/10/07	Mon 8/20/07
20	Piles	Tue 7/10/07	Mon 8/20/07
21	Foundations	Tue 7/24/07	Mon 10/1/07
22	Underslab Utilities	Wed 9/5/07	Tue 10/16/07
23	Slab-on-Grade	Mon 10/8/07	Mon 12/31/07
24	CMU Walls	Mon 10/22/07	Mon 1/28/08
25	Structural Steel (incl. Joists & Decking)	Mon 12/10/07	Fri 2/29/08
26	Elevated Slab	Thu 1/31/08	Wed 2/13/08
27	Roof	Thu 2/21/08	Fri 5/9/08
28	Exterior Skin & Windows	Thu 1/31/08	Fri 5/16/08
29	Mechanical	Mon 11/19/07	Tue 7/29/08
30	Electrical	Mon 11/19/07	Tue 7/29/08
31	Interior Walls	Thu 2/14/08	Mon 6/30/08
32	Finishes	Thu 5/1/08	Tue 8/12/08
33	Final Cleaning	Mon 7/28/08	Fri 8/22/08
34	Substantial Completion	Wed 8/13/08	Wed 8/13/08
35	**MIDDLE SCHOOL**	**Tue 7/17/07**	**Wed 10/15/08**
36	Earthwork	Tue 7/17/07	Mon 8/27/07
37	Piles	Tue 7/24/07	Mon 8/27/07
38	Foundations	Tue 7/31/07	Mon 10/1/07
39	Underslab Utilities	Wed 9/12/07	Tue 11/13/07
40	Slab-on-Grade	Wed 10/24/07	Tue 1/1/08
41	CMU Walls	Wed 11/21/07	Tue 2/12/08
42	Structural Steel (incl. Joists & Decking)	Mon 1/7/08	Fri 4/18/08
43	Elevated Slab	Mon 2/25/08	Fri 4/4/08
44	Roof	Mon 3/17/08	Mon 6/9/08
45	Exterior Skin & Windows	Mon 2/25/08	Mon 6/16/08
46	Mechanical	Mon 2/4/08	Wed 9/3/08
47	Electrical	Mon 2/4/08	Wed 9/3/08
48	Interior Walls	Mon 3/17/08	Tue 7/29/08
49	Finishes	Mon 5/19/08	Wed 9/17/08
50	Final Cleaning	Thu 9/18/08	Wed 10/15/08
51	Substantial Completion	Thu 10/2/08	Thu 10/2/08

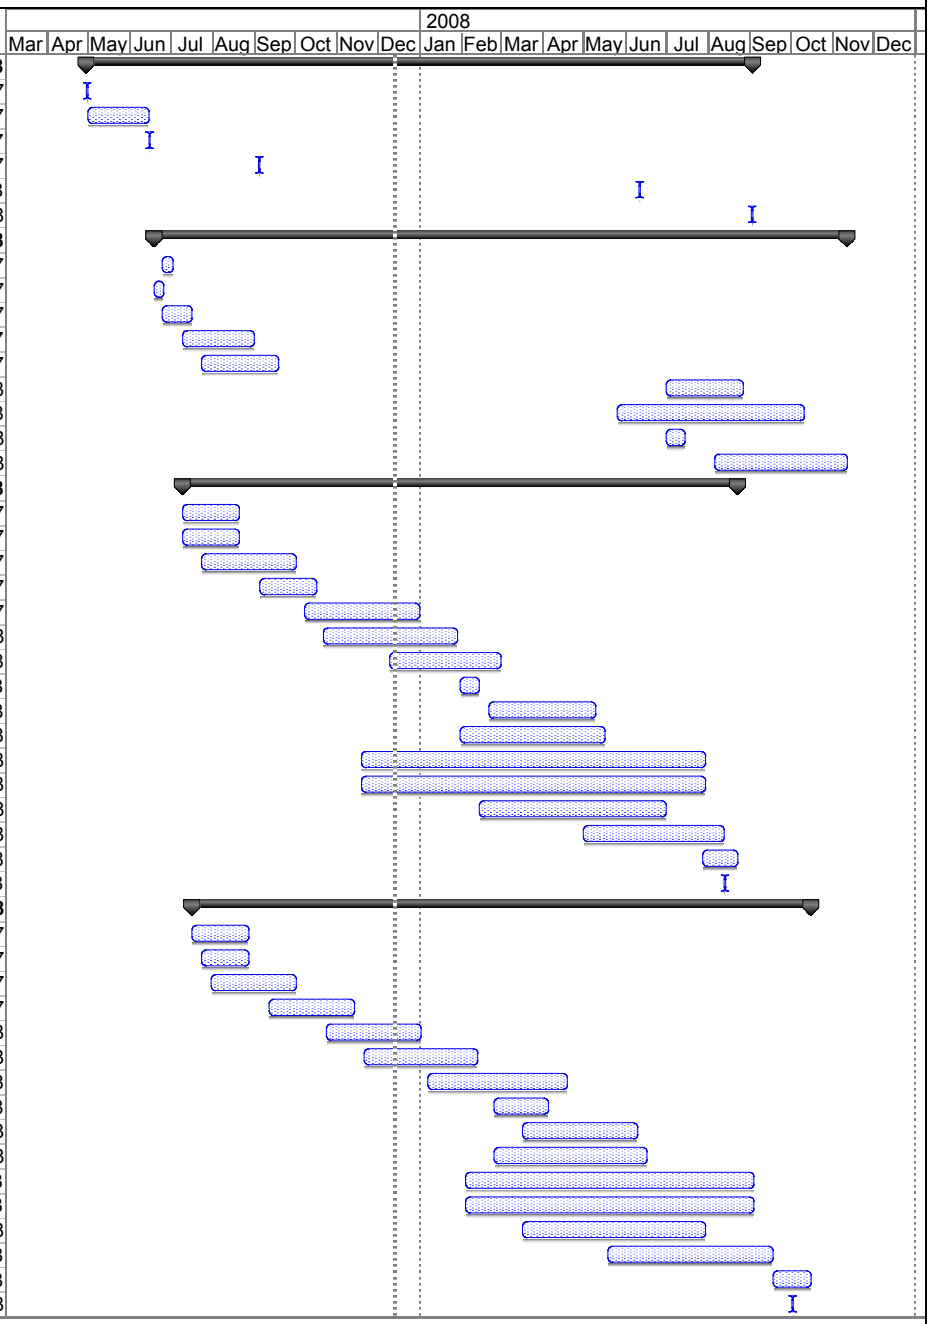

Project: HV ES MS Website Sched up
Date: Thu 12/13/07

Task
Progress
Milestone
Summary
Rolled Up Task
Rolled Up Milestone
Rolled Up Progress
Split
External Tasks
Project Summary
Group By Summary
Deadline
